



Fantastic 14

Exam Session
Sprint 5 & 6

14 & Attraktor

Agenda



- Introduction
- Product goal
- Ways of working
- Spent and remaining effort
- DoD
- Software qualities
- Sprint results
- Software demo
- Collaboration
- Realized project scope
- Complicating and simplifying factors
- Evaluation of used work practices and tools

Introduction to the project



- We have been tasked with making new features for the Tastelater website.
- Our job was the creation of a transaction register for each relevant user role.
- We also had to make a dashboard so the admins can get a proper understanding of the financial state of their business.

Product Goal



- Current Tastelater
- Extend with new financial tracking system
- Userflow for Admins, Consumers, and Suppliers
- Tracking of payments, and cashflow (with VAT handling)
- Per-role personalized transaction register
- Finance dashboard for admins
- Financial health of the company

Team's Ways of Working



- Sprint schedule
 - Sprint planning
 - Daily scrum
 - Backlog refinement
 - Sprint review
 - Sprint retrospective
- Changes since the previous session – none

Sprint Schedule

	MAN.	TIRS.	ONS.	TORS.	FRE.	LØR.	SØN.
week 1	Sprint Planning			Daily Scrum			
week 2	Daily Scrum			Sprint Review & Retrospec			

Spent and Remaining Effort



	Emil	Noah	Adam	Bárdur	Mathias	Sif	Simon	David	Allan	SUM
Project Kickoff	10	14	10	10	10	10	10	10	20	104
Sprint 1	26	28	24	29	20	25	19	19	27	217
Sprint 2	25	24	26	28	24	24	30	29	12	222
Sprint 3	27	34	36	30	28	21	39	20	12	247
Sprint 4	16	46	32	21	13	14	53	15	12	222
Sprint 5	18	31	19	16	13	16	38	20	15	186
Sprint 6	33	50	11	16	18	9	50	10	9	204
Total	155	227	158	150	126	119	239	123	105	1402

(Spent hours)

Definition of Done



- Main points
 - Tested issues in review has to be shown to PO and accepted by PO, or accepted by other developer, given PO's responsibilities temporarily.
 - Software Qualities are followed.
 - Unit tests. Happy path and bad path tests. All tests are peer reviewed.
 - Readable. Peer reviewed by at least 3 developers, of which, at least 1 has not been involved at all.
 - Code in alignment with the SOLID principles (Single responsibility principle, Open-closed principle, Liskov's substitution principle, Interface segregation principle, and Dependency inversion principle).
 - Automated tests cover critical paths (order calculations, VAT calculation, transaction numbering).
 - Basic brief documentation in code comments and commit messages.
 - Merge changes into pre-release branch.
- How well has it been followed?
- Has it changed?

Software Qualities




- (Security) (FR) Critical parts of the system are calculations where there are monetary risks. These calculations should be thoroughly tested.
- (Security) (FR) Authentication and role-based access control ensure that only authorized users can access sensitive financial data.
- (Maintainability) (NFR) The code is clean, well-documented, and structured for easy updates and future integration.
- (Functional Suitability) (NFR) The application should be correct in terms of its functionality.
- (Maintainability) (NFR) The application should be scalable in the sense of new cities (managers).
- (Performance Efficiency) (NFR) The application is designed to handle an increasing volume of transactions and additional user classes.

Sprint 5 – Results



- Sprint Goals: “
 - 1) Orders affecting/creating transactions
 - 2) Fake test data
 - 3) Shared date range selection between dashboard and register
 - 4) Consumer transaction register
 - 5) Playwright”

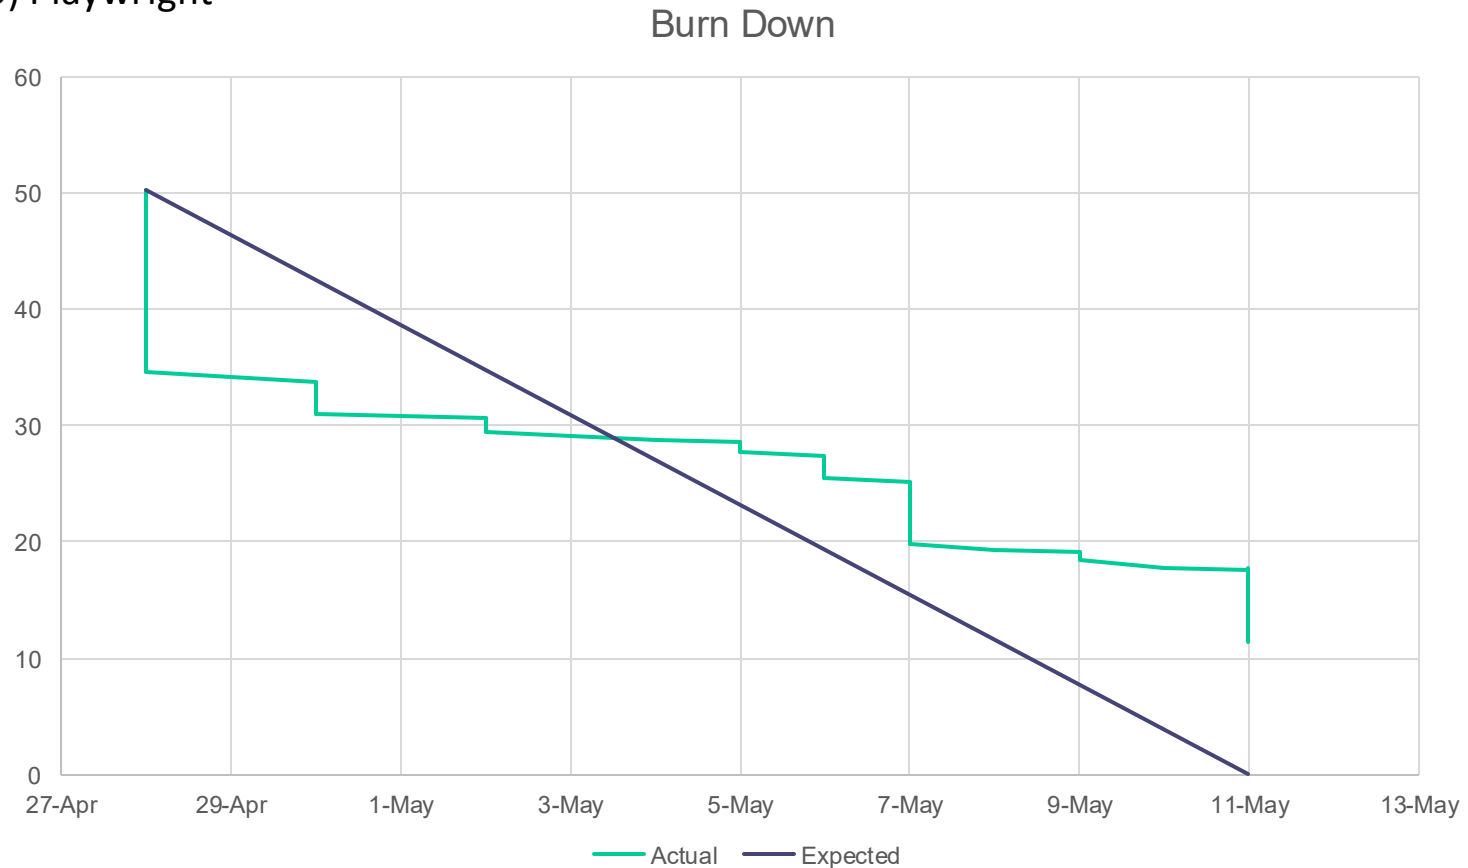

Sprint 5 – Retrospective




- Scheduling issues with PO.
- Sprint 5 review + retrospective & Sprint 6 planning simultaneously.
- Forgot the retrospective.

Sprint 6 – Results



- There wasn't a specific sprint goal for this sprint.
However, the plan was to finish up all remaining tasks, polish the product, and work on the report.
- We managed to get everything done, with all user stories active being marked as done!

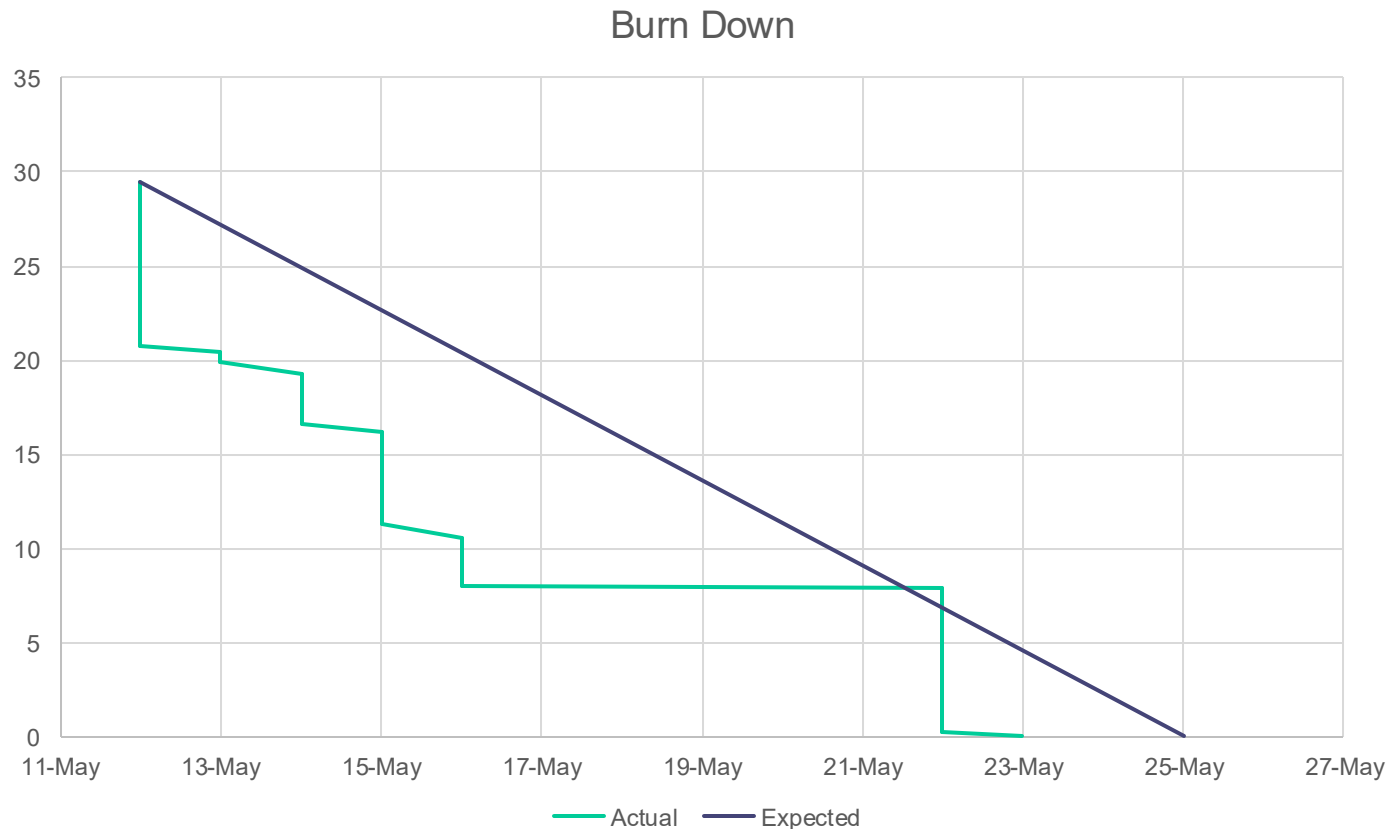

Sprint 6 – Retrospective



Find Retrospective

Timeline

Timeline - User A¹

Noah's Timeline

Sif's Timeline 16

Adam Timeline 3

Simon's Timeline 1

Timeline from 6

P.O. timeline

Emil's Timeline

Timeline - David 5


Baron's Timeline

Themes:

- Physical/virtual
- Linear
- Scrum - Value
- User- and business
- Understanding
- Dependencies
- Testing
- Interface
- Pre-release reviews
- Modular
- Playwright
- Book of System
- Enrich
- Unit Data
- VAT
- Refactoring
- GitHub
- Schedule

Timeline

Timeline - Allan



Leader of Finnish / Czech mate!

Dot voting

Future considerations

Lessons learned

Problem areas

Accomplishments

Human level

Guilty pleasure

Set-up

My music videos be more entertaining.... I guess

In my case the availability towards the end (when it is the most important)

You don't need meetings with SM

Glossary must be reviewed... yesterday!

It works hybrid. It works remote too

PO sending funny meme

Realizing its about you

Manager telling us we are family

Me who has applied to 30 other families this week

Software Demo



Tastelater

Hello, developer@dev.com! [Log out](#)

- Personal Info
- Dashboard
- Transactions
- Ingredients
- Users
- Kitchens
- Suppliers

Date range

Financial Dashboard			
	Operative	Expected	Unpaid
Income	0.00	98.76	98.76
Expense	-98.76	0.00	0.00
Balance	-98.76	98.76	98.76
VAT Estimate	-24.69	24.69	24.69


14/05/2025 09:39:22				Paid	
ID	Address	DeliveryTime	Timeframe	Distribution	Status
1	Consumer Street 1, Consumer City, 0001	16/05/2025 09:39:22	12:00-14:00	Delivery	Active

Collaboration / sharing / learning with and from other teams



- We participated in an experience exchange.
- We heard that meeting with the previous team who handled the project is a good idea
- We shared our experience of how to handle an indecisive PO
- We shared how we do pull request with peer review and about setting up rules for the pull requests.

Realized Project Scope vs. Original/Updated Product Goal

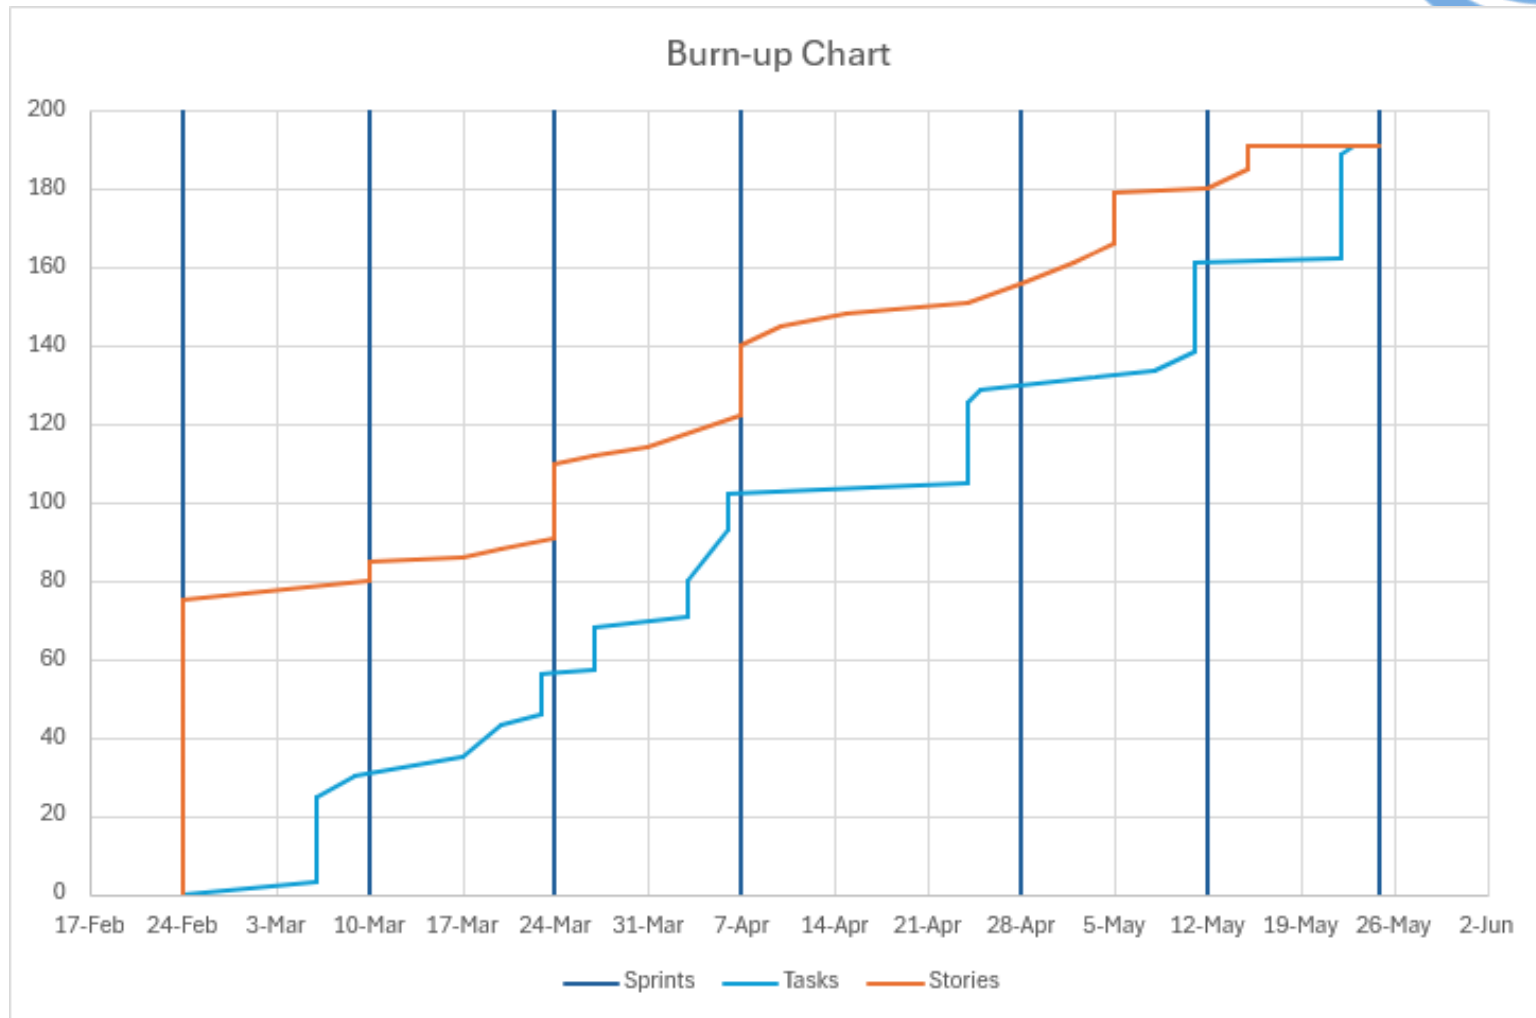

Complicating and Simplifying Factors



Complicating factors

- The use of bUnit – we were all new to this test suite
- Having our PO be strictly online and moving to fully virtual meetings
- 6 different electives caused scheduling conflicts
- Communication sometimes breaking down (specifically in regard to progress of tasks)

Simplifying factors

- We had all worked on a project of similar structure before using Razor Pages
- There has been no internal strife
- Karen & Thomas
- Allan

Evaluation of Used Work Practices and Tools



- Peer review code – having multiple people review pull request
- Star fish model – was good way to reflect
- Flap & Timeline – was an interesting way to gain perspective over the entire project
- Roman voting – made it easier to make group decisions
- Passing the ball – allowed everyone to have a say
- Linear & Excel – for tracking work
- Discord – for communication
- Change in how we estimate user stories/tasks
- Going from physical to virtual meetings
- Stand ups/Daily scrum – due to moving to virtual meeting, we had a lack of communication and status reporting
